


# Building Report | E/W Tech Renovations & Addition

5.10.19

The following are pictures from week of 5.6.19 - 5.10.19 in regards to the East/West Technology Buildings Renovations and Addition Project. Demolition (both interior and exterior) is progressing nicely. A lot of walls have come down and/or are in the process of coming down in West Tech. Next week we should some walls start coming down in East Tech as well. The roof restoration portion of East Tech has started. So far all of the ballast has been removed, and the contractor is carefully removing the old built-up system (layers of felt, asphalt, and insulation) and replacing it with the new hybrid system (layers of membrane, asphalt, and insulation) removing and replacing what can be done while protecting the building below from all the rain we have received lately. Additionally, a fair amount of the coping along the roof perimeter has been replaced per the architect's drawings as well. Next week we should some demolition start in between the two buildings as the existing storm water system there is removed in preparation for the addition to be constructed later.

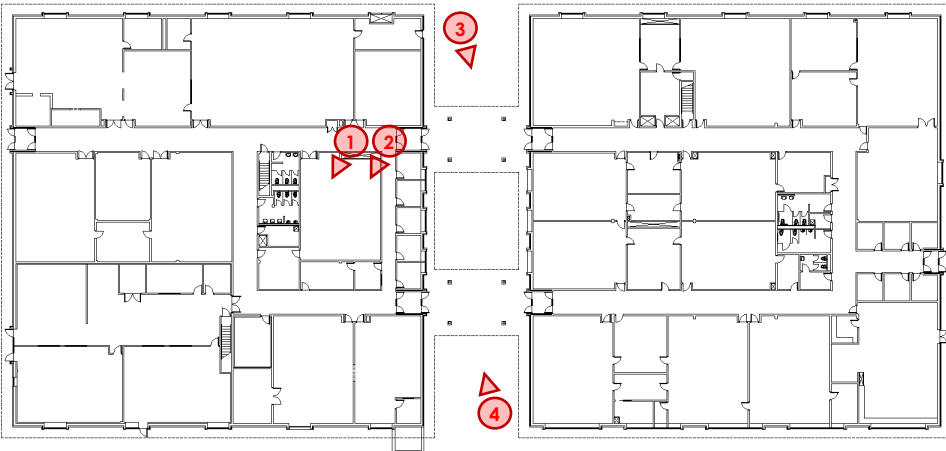

Again, using the old floor plans for East and West Tech marked for reference I have placed numbered arrows where I have taken photographs for orientation purposes. Photos 1 & 2 are taken in the same location so you can see before and after all the walls of the east bank of offices in West Tech and the adjacent classroom after they were removed. You can see beyond the walls in the old Wine Lab and Classroom starting to come down as well. Photos 3 & 4 show the demolition of the existing canopies that used to connect East and West Tech either removed or being removed along with a fair amount of the existing fascia and soffit. This work is all in preparation for the construction of the addition starting in the next few weeks.



# Building Report | E/W Tech Renov. & Addition [cont.]

## 5.3.19



Photo #5 shows the progress of the demolition in the old Welding Lab. A lot of the ventilation and electrical systems are down or are in the process of coming down. Photo #6 is in the one of the old Data Processing offices. Here you can see the installation of a new wall-mounted mini-split HVAC system being installed that will cool this space while the server in the old Data Processing Server Room are temporarily relocated during abatement/renovation. Photo #7 shows progress in another room in East Tech where finishes (floors and ceilings) have been removed as part of the overall renovation plan. Photo #8 is not shown on the map, but is taken from the 2nd floor of the CLRC looking towards East Tech. The photo shows the progress of the roof restoration.

