

Building Report | E/W Tech Renovations & Addition

5.17.19

The following are pictures from week of 5.13.19 - 5.17.19 in regards to the East/West Technology Buildings Renovations and Addition Project. More and more trades are showing up as demolition work continues with this project. The roofing sub-contractor is slated to complete the replacement of the roof over what is now East Tech sometime next week. Both the mechanical/plumbing and electrical subs are on site as well removing existing equipment and associated piping, electrical, etc. as needed to accommodate the proposed new building layout. The demolition contractor is making great headway with the demolition required in both buildings. More walls have come down in West Tech and next week there will be some coming down in East Tech as well. The steel shop drawings were just approved so in roughly six weeks the structure for the addition will start erection. Finally, the server in the old Data Processing area was successfully moved to it's temporary location meaning the space it was in can now be abated and the demolition required completed.

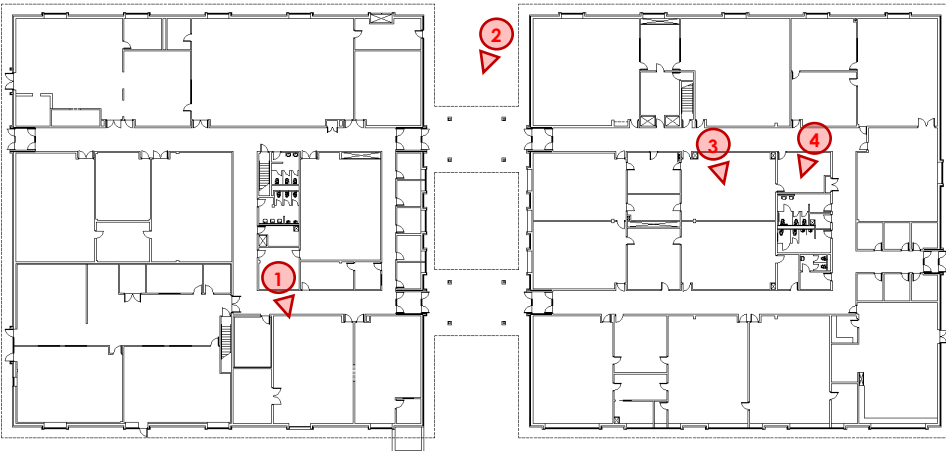


Photo #1 shows the nearly completed removal of the walls in the old Wine Lab and Classroom area. Photo #2 shows the completed removal of the fascia panels, soffit, roof, and supporting steel structure along the east side of West Tech. The smaller overlapping photo shows the similar process happening on the mirrored face of East Tech. Photo #3 and the overlapping photo show the removal of the raised flooring system in the old Data Process Server Room. This room can now be abated which will start next week. Photo #4 shows the computer server that once was in the old Data Processing Server Room in it's temporary location. The second and final move for this system will be into adjacent space which will be the new server room when completed.



Building Report | E/W Tech Renov. & Addition [cont.]

5.17.19



Photo #5 is East Tech in the CIS classroom/lab area where two separate rooms are being combined into a shared storage space. Photo #6 shows some mechanical demolition that has been finished in preparation for some major wall demolition that will be happening in this area soon. Here all of the old offices will be removed as this area will become a prep/storage room for the adjacent art classrooms and labs. Photo #7 is an aerial view of the roof work happening over East Tech. The work here is a complete removal of the old built-up roof and the installation of a new hybrid built-up system. This work is set to be completed next week. Photo #8 is a good view of the demolition and prep work being done in between the two buildings.

