


Building Report | CLRC Renovations and Additions Project

06.24.22

The following are pictures from the week ending in 06.24.22 in regards to the CLRC Renovations and Additions Project. The installation of the furniture is full swing offices, classrooms, commons areas, etc. all steadily being populated. Additionally, numerous areas are receiving final finishes like wood trim, wall base, and tackable wall surfaces. There is one last minor electrical shutdown in the planning process that will only affect a small portion of the building, and that is so the new UPS (uninterruptable power supply) unit can be installed in the server room in the basement. This unit protects all the sensitive computer equipment in there by "cleaning up" the power from our local utility. It also acts as a bridge in the case of an outage before the generator can kick in and provide the necessary emergency electrical supply. More work was finished on the canopies with only the undersides left to be finished. Site clean up started with a majority of the temporary fencing coming down and the beginning of the landscaping work starting.



The top-right photo shows the now completed ceiling in the main area of the Learning Resources Center (library). You can see all of the boxed furniture sitting below which will start to be assembled and installed next week.

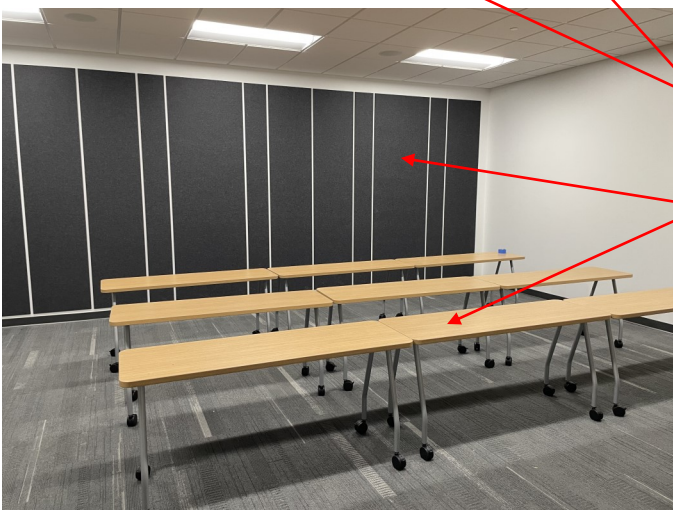

The top-left photo shows the progress of the installation of the new glass railings and stair tread coverings in the east stair tower.


The bottom-left photo was taken in one of the classrooms on the second floor and shows the beginning of the furniture installation in the foreground. The tables are in and next week the complimentary chairs will arrive. In the background you can see an installation of some acoustic tackable surface.



The bottom-right photo highlights the beginning of the installation of the furniture in the H/SS Division Office Suite. Featured in this photo are the hoteling stations that will be available for the adjunct faculty. These stations will be populated with computer stations so the adjunct faculty can have access to electronic resources before, in between, or after their classes.

Building Report | CLRC Renovations and Additions Project

06.24.22

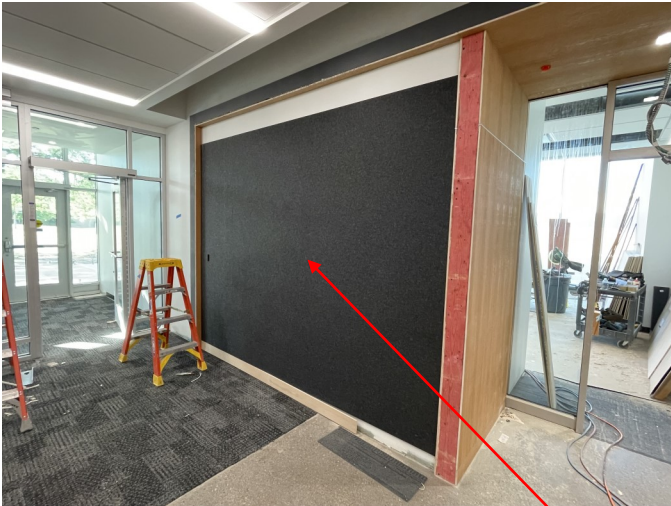

The top-right photos was taken in the active learning classroom on the 2nd floor and shows the beginning stages of the installation of the A/V infrastructure and the group learning tables.

The top-left photo shows the area near the new east entrance on the 2nd floor where some more tackable surface has been installed.



The middle-left photo was taken in the Adjunct Faculty Office in the H/SS Division Office Suite. The adjustable shelving will serve as mail slots for the adjunct faculty, and the filing cabinet will provide secure storage for files for the part-time instructors.

The bottom-right photo shows the now installed overhead coil-ing gate and surrounding finished wood trim at the entrance to the Learning Resources Center (library) on the 1st floor.



The bottom-left photo highlights more of the progress of finishing the new entrance canopies. Here you can see the coping has been installed around the perimeter of the roof. Up next the contractors will focus on installing the LED lighting, and finishing the underside with synthetic stucco system that will match the existing soffit of the building.

