
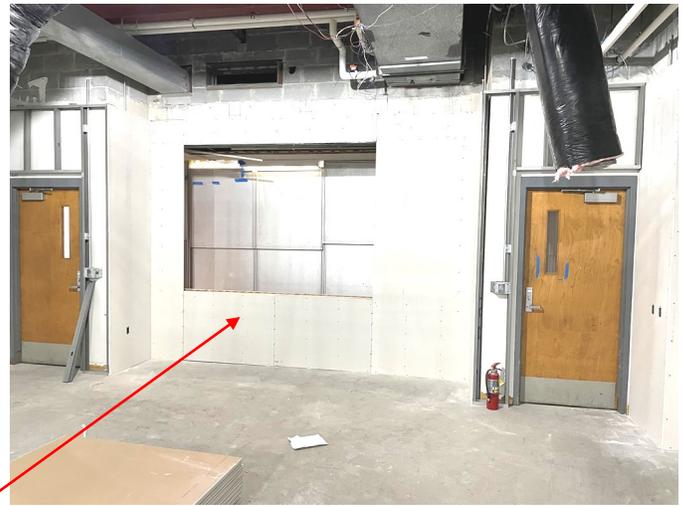


# Building Report | DEI Ctr./Stud. Govt. Room Renovations

10.29.21

The following are pictures from the week ending in 10.29.21 in regards to the Diversity, Equity, and Inclusion Center (DEI)/ Student Government Room Renovations Project. The in-wall electrical installation has been approved and now wall-board is starting to be installed. The contractors focused more this week in the Student Government Room, especially around the area that will be the office. Next week they will move over to the DEI Center side of the project. Also the sound insulation installation for the wall between the new Student Government Room and the existing adjacent Data Processing/Institutional Research Office will take place. This is so that there will be a definite sound barrier between the two spaces for obvious noise control reasons. Once the wallboard is complete in both spaces the contractors will begin the process of finishing it by taping and mudding the joints so that it can ultimately be painted as directed.

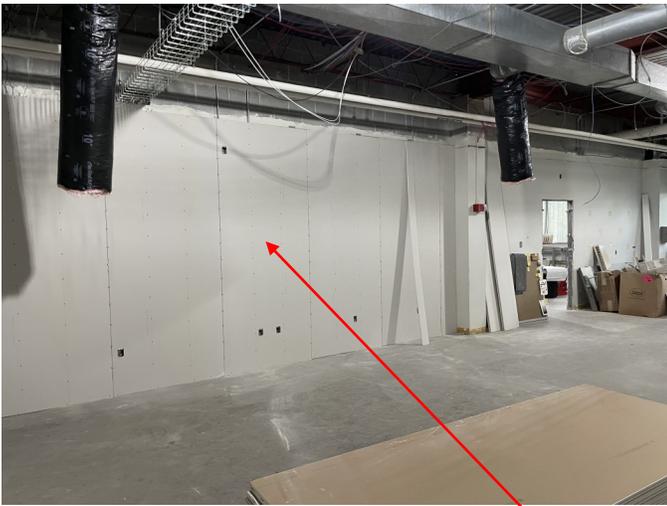

The top-right photo shows the north wall of the Student Government Room and the newly installed wallboard.

The top-left photo is similar to the top-right photo as it shows the wallboard installed over the metal furring strips on the east wall that is shared with the DEI Center being constructed in the adjacent area.

The bottom-left photo highlights the future office in the Student Government Room as it has now received its wallboard.

