

# Building Report | Campus-wide IT Rooms Renovations

## 8.2.19

The following are pictures from week of 7.22.19 - 8.2.19 in regards to the Campus-wide IT Rooms Renovations Project. This project is progressing well as each of the new IT Rooms has been started, with a few nearly complete. All demolition and new masonry associated with this project is complete, and all new wall framing is finished as well. A lot of new areas of gypsum board (drywall) has been installed or is nearly finished. Painting is partially complete and a fair amount of other finishes needed have been started. Numerous new doors and frames will be installed in the next week and then will receive paint or stain shortly thereafter. Some of the new technology infrastructure items have been installed as well such as ladder racks and cable trays that will hold the new cabling that will be installed later. New HVAC systems and electrical gear are being installed that will power the equipment in these rooms. These new rooms will finish up shortly which will allow some other millage projects to begin.



Photo #1 shows the progress of the work in the IT Room on the 2nd Floor of the Physical Plant. The new wall separating the new IT Room from the new dedicated mezzanine area has been constructed, and the door frame installed. Next up for this area is the insulation for the exterior walls and the new steel access stairs.

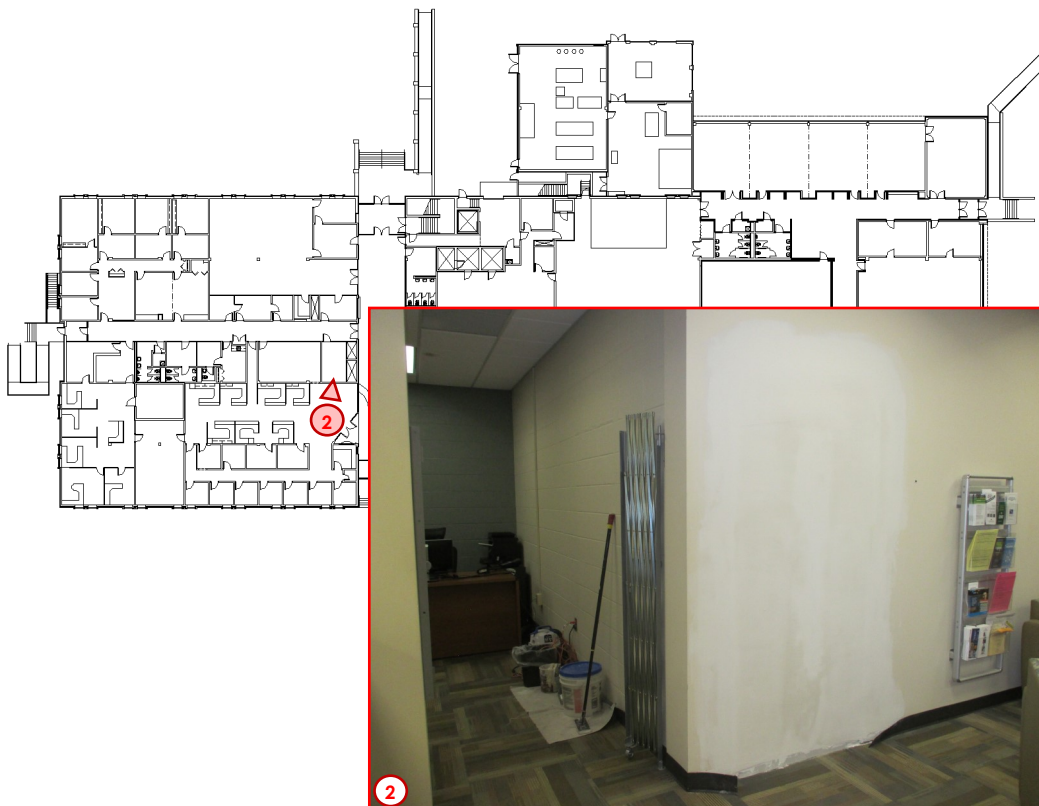


Photo #2 is in the Administration Building near the Admissions Office where the two old doors have been removed and covered. The only parts left are to paint the walls and install new wall base.

# Building Report | Campus-wide IT Rooms Reno. [cont.]

7.12.19

Photo #3 is in the Scene Shop of the La-Z-Boy Center where a whole new IT Room is being constructed. The walls and their foundation are finished and soon the concrete and steel deck cap will be installed.

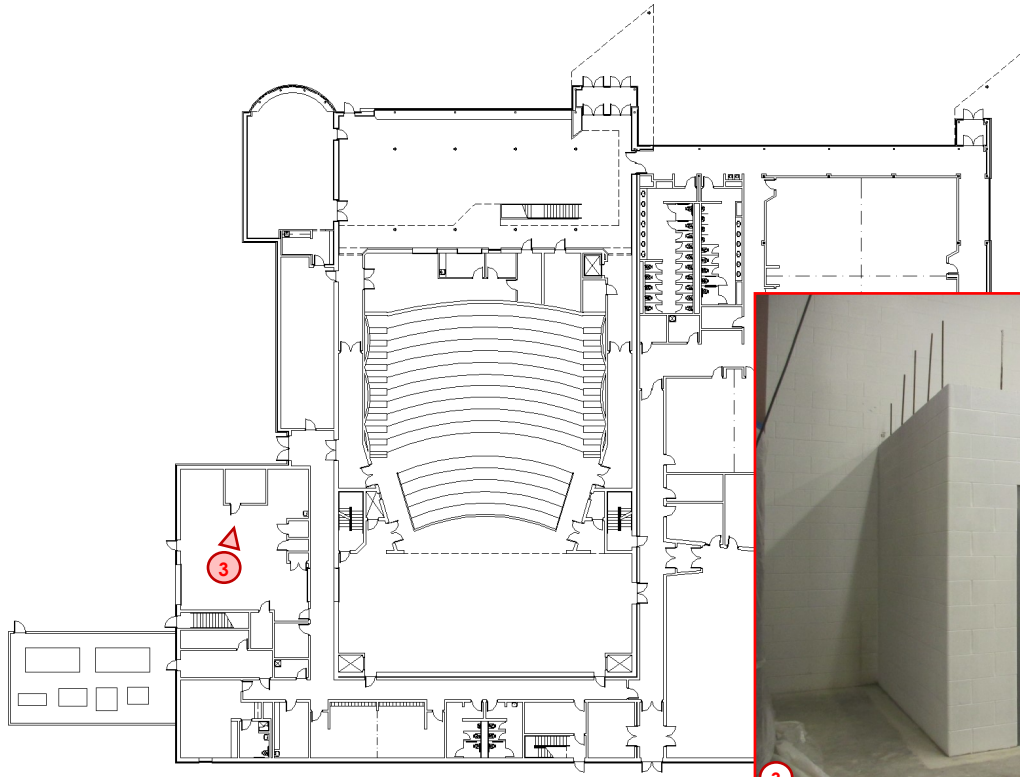


Photo #4 shows the progress of the conversion of an existing space in the Health Education Building off the Atrium into the new IT Room. The new separation wall is nearly complete, and soon the necessary infrastructure for the future electronics will be installed.

