

# Building Report | Little Theater Renovations

10.25.19

The following are pictures from week of 10.21.19 - 10.25.19 in regards to the Little Theater Renovations Project. This project is just getting underway and thus far is progressing very well. There was an unexpected area where some asbestos abatement had to be dealt with fortunately a qualified abatement contractor was able to come in right away and clear the area properly and keep the project on schedule. All the work that happened this week was demolition which will carry over into next week. Thus far demolition has been removing the old seating, carpeting, ceiling tile and grid, and stage curtains and rigging. Next week the electrical contractors will be in to remove the existing lighting—both house and stage, along with the old A/V wiring. Additionally, some new construction will occur as the carpenters will be to start constructing the two new ADA compliant ramps that are a major part of this project.

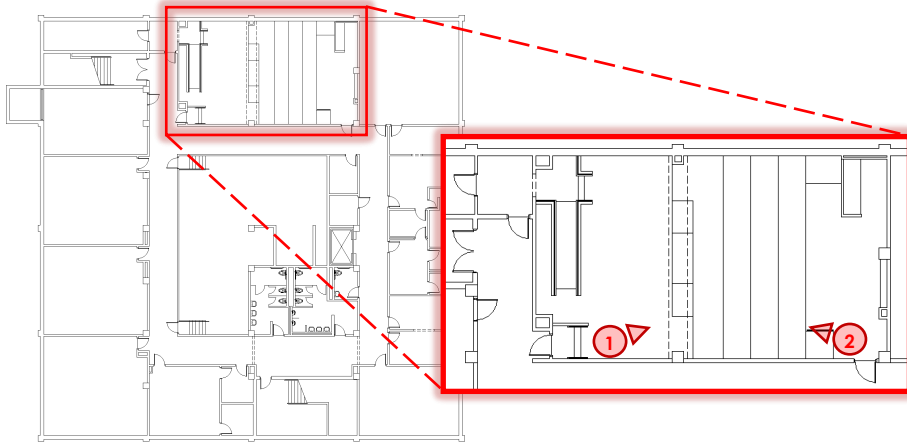


Photo #1 was taken from the stage looking towards the back of the theater. Thus far the existing seating, carpet, tech booth, ceiling grid and tile, and wall-mounted acoustic panels have been removed. Photo #2 was taken from the back of the theater looking towards back of the stage. There the first portion of the old ramp has been removed along with all the existing curtains and associated rigging.

