

Building Report | Little Theater Renovations

11.1.19

The following are pictures from week ending in 11.1.19 in regards to the Little Theater Renovations Project. This project is moving fast as demolition is complete and new construction progresses. This week framing for the new ramp at the back of the stage started. Additionally concrete was placed at both the top and bottom of the tiered seating area. The new concrete will be for the ramp at the front of the seating area, and then to create a walkway in the seating at the back of the room. The necessary paperwork was completed and the new seats are on order and should arrive and being installed towards the end of this project as planned for the first part of December. Over the next few weeks a lot of trades will be on site working on this project so the transformation for this space will happen rather quickly.

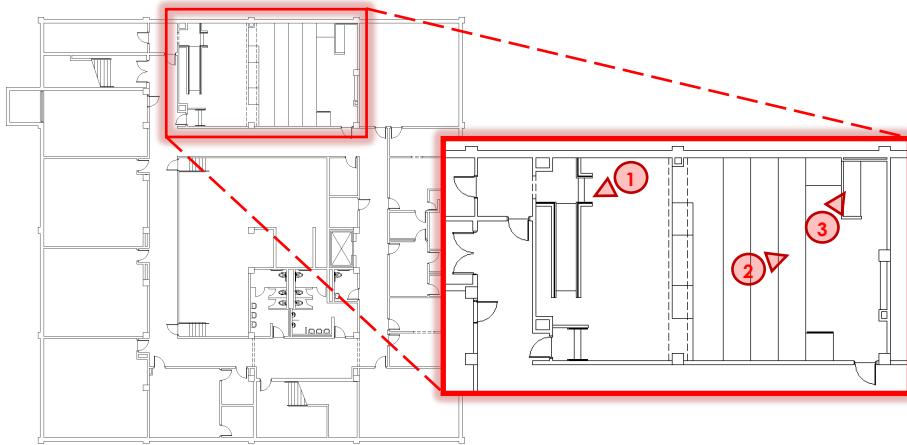


Photo #1 shows the progress of the framing required for the new ramp at the rear of the stage. Photo #2 shows the contractors placing and finishing the new concrete for the expanded aisle way in the seating area towards the rear of the theater. Photo #3 shows the area where the new tech booth will be placed and some of the new electrical infrastructure (the conduits on the wall) that service the new A/V equipment. These conduits will be concealed in a yet to be erected chase.

