

# Building Report | Little Theater Renovations

11.15.19

The following are pictures from week ending in 11.15.19 in regards to the Little Theater Renovations Project. The framing for the new ramp and stairs is nearly complete. Interior contractors will be on site this week to prep and paint the new wall board as well as the open ceiling area above the stage. There was a small area of additional demolition that needed to happen towards the back of the seating area in front of the new control booth. This demo was necessary to make the new aisle ways work with the proposed seating layout. Wiring for all of the new A/V and room lighting will start this week or at least early next week. The new ceiling grid for the ceiling above the seating area should start this week as planned. The remainder of the trim work for entry at the top of the ramp at the back of the stage will be completed soon. Thus far this project is still on track for an early December completion.

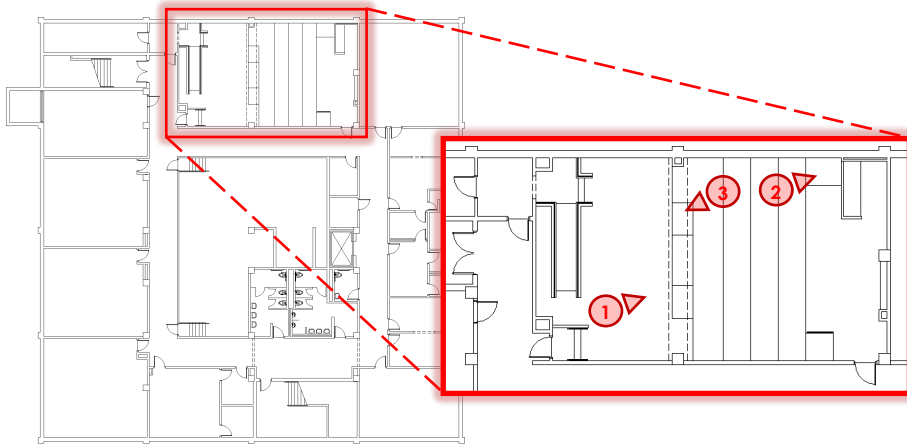


Photo #1 shows the wall board now installed over the new metal stud framing. This wall board can now be finished and painted. Photo #2 shows a small area of demolition of the existing tiered concrete floor. This demo was needed so that the new cross aisle that was installed works with the side aisles and the proposed seating layout. Photo #3 shows more of the finish work happening with the stage framing concerning the new ramp. The side wall sheathing and wall cap for the ramps have been installed and both areas are awaiting finishes (paint, etc.).

