

# Building Report | Little Theater Renovations

11.29.19

The following are pictures from weeks ending in 11.22.19 and 11.29.19 in regards to the Little Theater Renovations Project. The framing for the new ramp and stairs is nearly complete. As projected the progress for the work associated with this interior renovation is moving quickly as we look towards this space being completed in a very short amount of time. All of the new framing is complete, wall board installed, and the space is being painted. Up next will be the installation of the new ceiling and lighting, acoustical wall treatments, flooring, casework/millwork, and A/V components. All of these items will be installed prior to the arrival of the new seating which if all goes well will arrive and be installed next week. Again, this space will be completed and online for the first day of classes for the Winter 2020 Semester.

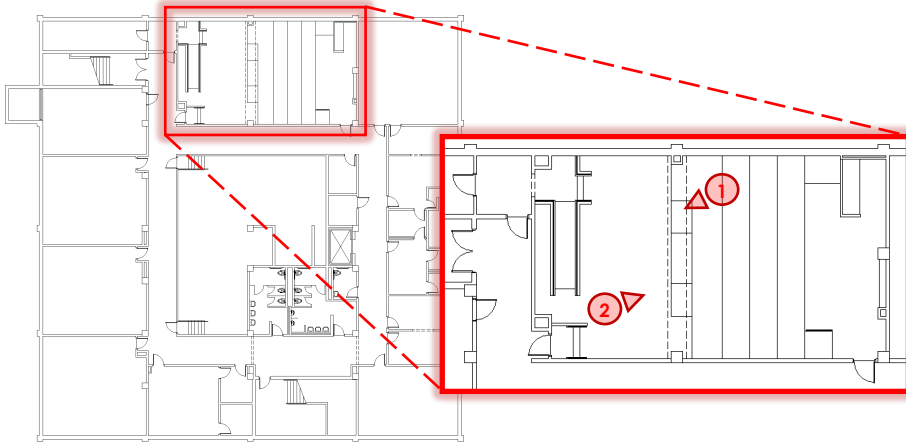


Photo #1 shows the now finished stage. The new ramp is ready has been framed, finished, and is ready for railings. The walls and open ceiling has been painted which will allow for the new A/V systems, lighting, and curtains to be installed. Photo #2 shows the seating area of the theater framed and painted. Next up the contractors will install the ceiling, acoustical wall treatments, casework/millwork, floor finishes, etc. in preparation for the arrival of the new seating. One can also see the new ramp in the foreground which means this space is now compliant with all current building codes which has not been the case for this space prior to this renovation.

