

Building Report | Little Theater Renovations

11.8.19

The following are pictures from week ending in 11.8.19 in regards to the Little Theater Renovations Project. This project is on target for completion as expected in the early to middle part of December. A number of key meetings and discussions were held this week dealing with the proposed casework (teaching station and A/V control booth), house and stage lighting, A/V systems (for both classroom and theater), and stage curtains and rigging so that materials and equipment can be ordered to stay on track with the overall construction schedule. A lot of framing was completed as well which combined with a lot of the electrical infrastructure being installed will allow for wall board to go up and finishing to start to take place. The delivery dates for the new seating has been confirmed.

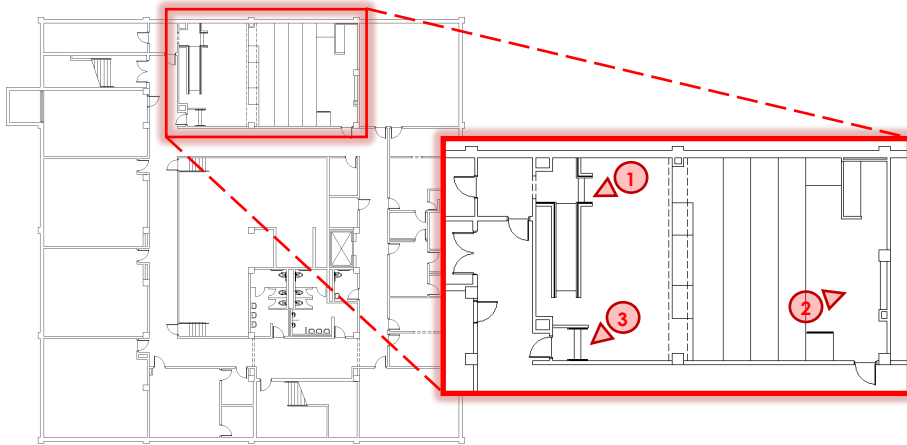


Photo #1 highlights the progress of the framing for the new ramp and stairs at the rear of the theater. Conversely the ramp at the front of the stage is nearly complete as well. When finished these new ramps will allow full access to the stage and teaching portion of this space. Photo #2 is a close up of the new metal stud framing at the rear of the theater for the new coat rack. Photo #3 shows the progress of the framing for the new partial height wall that will support the railing for the existing stairs at the rear of the stage.

