

Building Report | Little Theater Renovations

12.6.19

The following are pictures from week ending in 12.6.19 in regards to the Little Theater Renovations Project. It is hard to believe but by this time next week the Little Theater Renovations Project will be nearly complete with only a few punch list items left to be resolved. Carpet, seating, casework/millwork, stage curtains, and lighting will all be going in next week. All the prep work for the new A/V systems is in and that equipment will be installed next week. The new A/V equipment for this space will be a major upgrade from what was previously installed which will allow this space to be an even more effective teaching tool for the College. Additionally, this space will also be an asset to the community as it will provide another College provided space for community cultural outreach and enrichment.

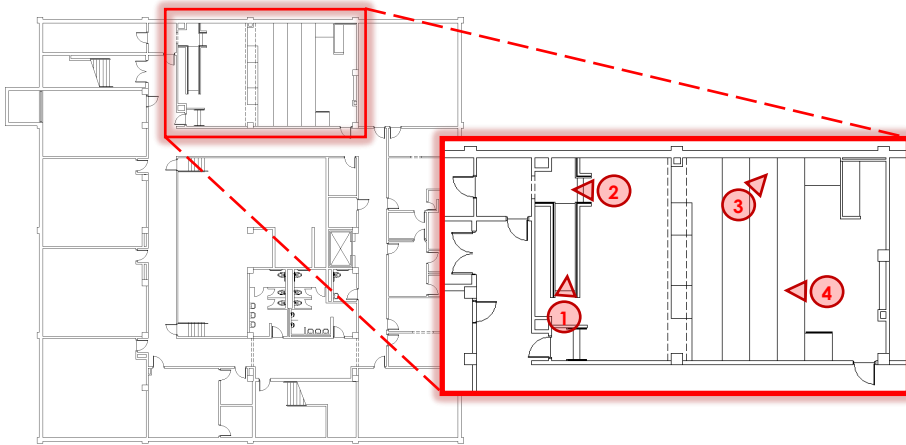


Photo #1 shows the handrails on the new backstage ramp that are now installed and complete this portion of the project. Photo #2 shows some of the finish carpentry work taking place. Here you can see the work needed to finish out the entry into the back vestibule at the top of the new backstage ramp/stairs. This trim work will be painted to match the surrounding wall. Photo #3 shows some of the new acoustical wall panels that were recently installed on the east, south, and west walls of the seating area. These panels not only help with acoustics, but are also help create interest and add texture to the space. Photo #4 shows the new suspended ceiling system being installed in the space. Here you can see the metal grid is finished and waiting the tile.

