


Building Report | Unisex Restroom/Private Room Project

11.5.21

The following are pictures from the week ending in 11.5.21 in regards to the Unisex Restroom/Private Room Project located in the Student Services/Administration Building. This project passed a few inspections this week with the rough plumbing first on the list. This meant the opening in the floor slab could be filled in which then allowed the remainder of the restroom wall framing to be installed. The bulkhead on the south side of both rooms that helps transition the existing ceiling into the new suspended ceiling system was completed and has already received its wallboard. Next week some of the rough electrical and mechanical work will take place and hopefully inspected. This will allow the next set of inspections to happen so that the wallboard can be installed. This project should wrap up early to mid December as planned.

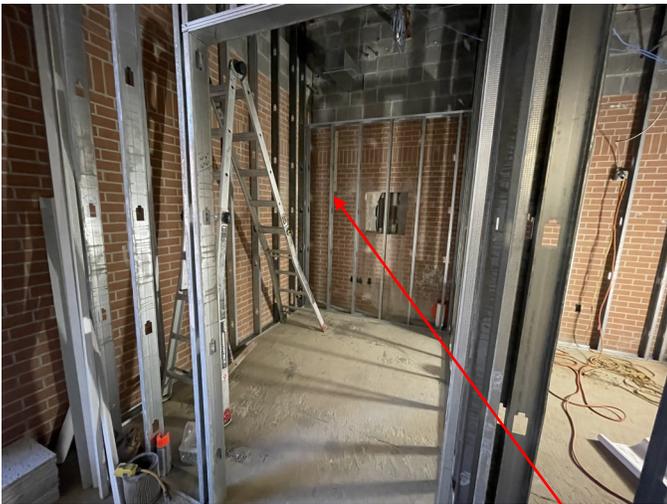

The top-right photo shows the new bulkhead in place that will help transition the new ceiling in this area into the existing. This bulkhead is needed because the existing spline ceiling tile system is no longer being produced or used and now a suspended acoustical tile ceiling system will be installed instead.

The top-left photo shows the now completed wall framing for the unisex restroom. Next week this will be inspected by local officials, and then the necessary electrical infrastructure can be installed.



The bottom-left photo shows the new patch installed in the floor slab, and once cured will be ready to receive the new ceiling tile floor finish slated for this room.
