

Building Report | Campus-wide Unisex Restrooms

11.29.19

The following are pictures from the week of 10.28.19 - 11.29.19 in regards to the Campus-wide Unisex Restrooms Installation Project. The two new unisex restrooms in the Life Sciences Building are pushing towards completion, and the locale in the CLRC basement is well underway and should be completed by the end of the month. The restrooms in the Life Sciences Building are both receiving finishes (mostly ceramic tile on both the floors and walls) now in preparation for the installation of the new plumbing fixtures. Some of the last items to be installed with these rooms will be the doors, electronic openers, etc. The basement unisex restroom has received its new ADA compliant door, and will start to see the new wall for the plumbing fixtures soon, and then will be finished out to match its counterparts. Again, these spaces will help the College meet ADA compliance as well as address other items such as the need for gender-neutral restroom facilities, restrooms that will allow for those students who require assistance, dedicated family restrooms, etc.

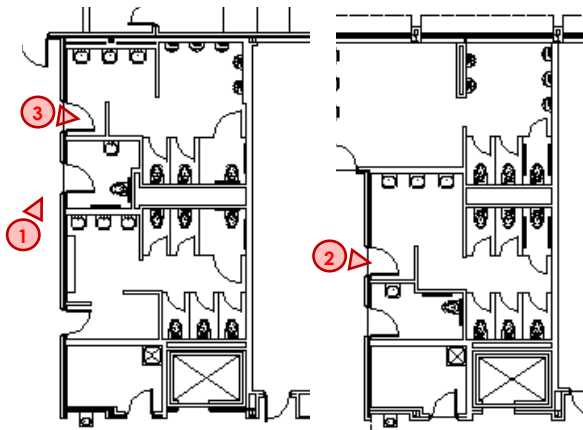


Photo #1 shows one of the two new completed ADA compliant doors, and adjacent restorative masonry work for the rooms in the Life Sciences Building. With this project two new doors and associated openings were required. Photo #2 highlights the installation of some of the new finish work being. All of the new ceramic tile being installed will match existing which was ideal for the college not only aesthetically, but also maintenance wise. Photo #3 shows an area where the new ceramic tile has been grouted and cleaned, and now that it is completed matches the adjacent existing tile. Photo #4 was taken in the CLRC basement (note: the plan is not shown to the left), and shows the now completed new ADA compliant door. Besides constructing a new masonry wall in the existing space, this new door was the most major component associated with the completion of this new restroom.

